

Isle of Palms Marina

Project Update – May 18, 2021

Current Progress



Current Progress




Current Progress



Current Progress



Current Progress

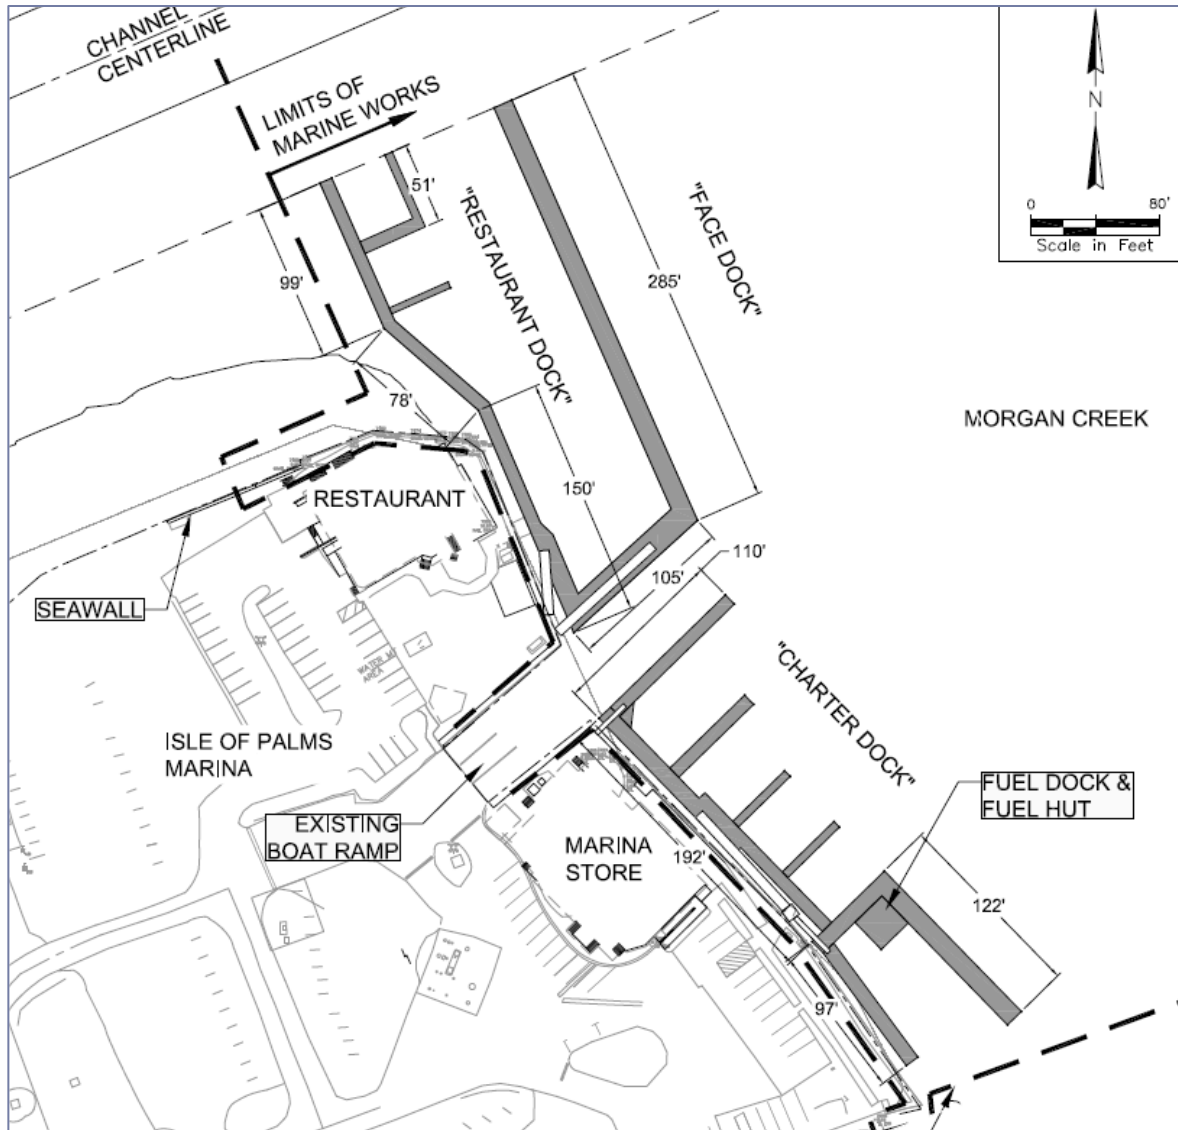

Schedule

▶ Dock Area C – “Restaurant and Face Dock”

- Demolition and Disposal of “C” May 10 – 17, 2021
- Offsite Mobilization/Loadout “C” May 18 – 21, 2021
- Mobilization and Installation of “C” May 24 – June 4, 2021
- Utilities Installation “C” June 4 – June 28, 2021
- Installation of Platforms & Gangways “C” June 28 – July 2, 2021
- Final Work to Place “C” in service July 6 – 9, 2021

Schedule

▶ Dock Area B – “Charter Dock”

- Demolition and Disposal of Dock “B” July 6 – 13, 2021
- Offsite Mobilization/Loadout Dock “B” July 14 – 16, 2021
- Mobilization and Installation of Dock “B” July 19 – 30, 2021
- Installation of Gangway Near Boat Ramp Dock “B” July 19 – 30, 2021
- Utilities Installation Dock “B” July 30 – 20, 2021
- Construction of Timber Platform Docks “B” & “A” August 2 – 11, 2021
- Installation of Gangway @ Timber Platform Dock “B” August 12, 2021
- Final Work to Place Dock “B” in Service August 16 – 20, 2021

Schedule

▶ Dock Area A “Fuel Dock”

- | | |
|--|--------------------------------|
| • Design Submittal Dock “A” | May 3 – June 11, 2021 |
| • Review of Dock “A” Design Submittal | June 14 – 18, 2021 |
| • Corrections & Revisions to Dock “A” Design Submittal | June 21 – 25, 2021 |
| • <u>Final Design Submittal Dock “A”</u> | <u>June 28 – 30, 2021</u> |
| • Material Procurement for Dock “A” Structure | May 17, August 13, 2021 |
| • Fabrication of Dock “A” Components | August 16 – September 3, 2021 |
| • Delivery of Dock “A” Components | September 10, 2021 |
| • <u>Pre-assembly of Floats at Salmons Terminal</u> | <u>September 13 – 22, 2021</u> |
| • Demolition and Disposal of Dock “A” | September 20 – 24, 2021 |
| • Mobilization to Install Dock “A” | September 27 – October 8, 2021 |
| • Installation of Gangway @ Timber Platform Dock “A” | October 6 – 8, 2021 |
| • Construction of Fuel Hut on Site | September 13 – 30, 2021 |
| • Installation of Utilities & Fuel Services for Dock “A” | October 1 – November 12, 2021 |
| • <u>Final Work to Place Dock “A” in Service</u> | <u>November 15-19, 2021</u> |
| • All Work Completed | November 19, 2021 |

Isle of Palms Marina

